

CRM Planning & Analysis - CPM and WBS Report

Kyrylo Pryiomyshev
30. October 2025

This report presents the planning and analysis phase for upgrading the internal Customer Relationship Management (CRM) System in compliance with new personal data storage regulations. The project employs the Work Breakdown Structure (WBS) and Critical Path Method (CPM) to identify the maximum duration required before development can begin.

Project Overview

As the Project Manager at QWERTY123, you are responsible for managing the planning and analysis of CRM updates. Since the task is high priority and resources are limited, effective scheduling and clear task dependencies are critical. This section summarises the project structure, roles, and assumptions.

Key assumptions:

- all durations are expressed in working days
- pre-project activities are excluded
- project and product teams can work in parallel where dependencies allow


Work Breakdown Structure (BWS)

The Work Breakdown Structure divides the planning and analysis into specific activities for both the Project and Product (System Analyst) teams. Each task is defined with its duration and prerequisites.

ID	Team	Task	Duration (days)	Predecessors
P1	Project	Define compliance scope and objectives	1	
P2	Project	Map stakeholders and data owners; confirm RACI	1	P1
P3	Project	Baseline project plan and WBS for analysis phase	1	P2
P4	Project	Perform risk assessment and mitigation planning	1	P2
P5	Project	Establish governance and obtain analysis go-ahead	1	P3, P4
SA1	Product (System Analyst)	Document as-is CRM data inventory and process flows	2	P1
SA2	Product (System Analyst)	Conduct legal gap analysis versus new personal-data law	2	SA1
SA3	Product (System Analyst)	Draft functional and non-functional requirements	2	SA2

ID	Team	Task	Duration (days)	Predecessors
SA4	Product (System Analyst)	Define data model updates and retention/consent policies	1	SA3
SA5	Product (System Analyst)	Prepare requirements traceability and acceptance criteria	1	SA3
P6	Project	Consolidate analysis, formal review, and handover package	1	P5, SA4, SA5

Activity Network Diagram

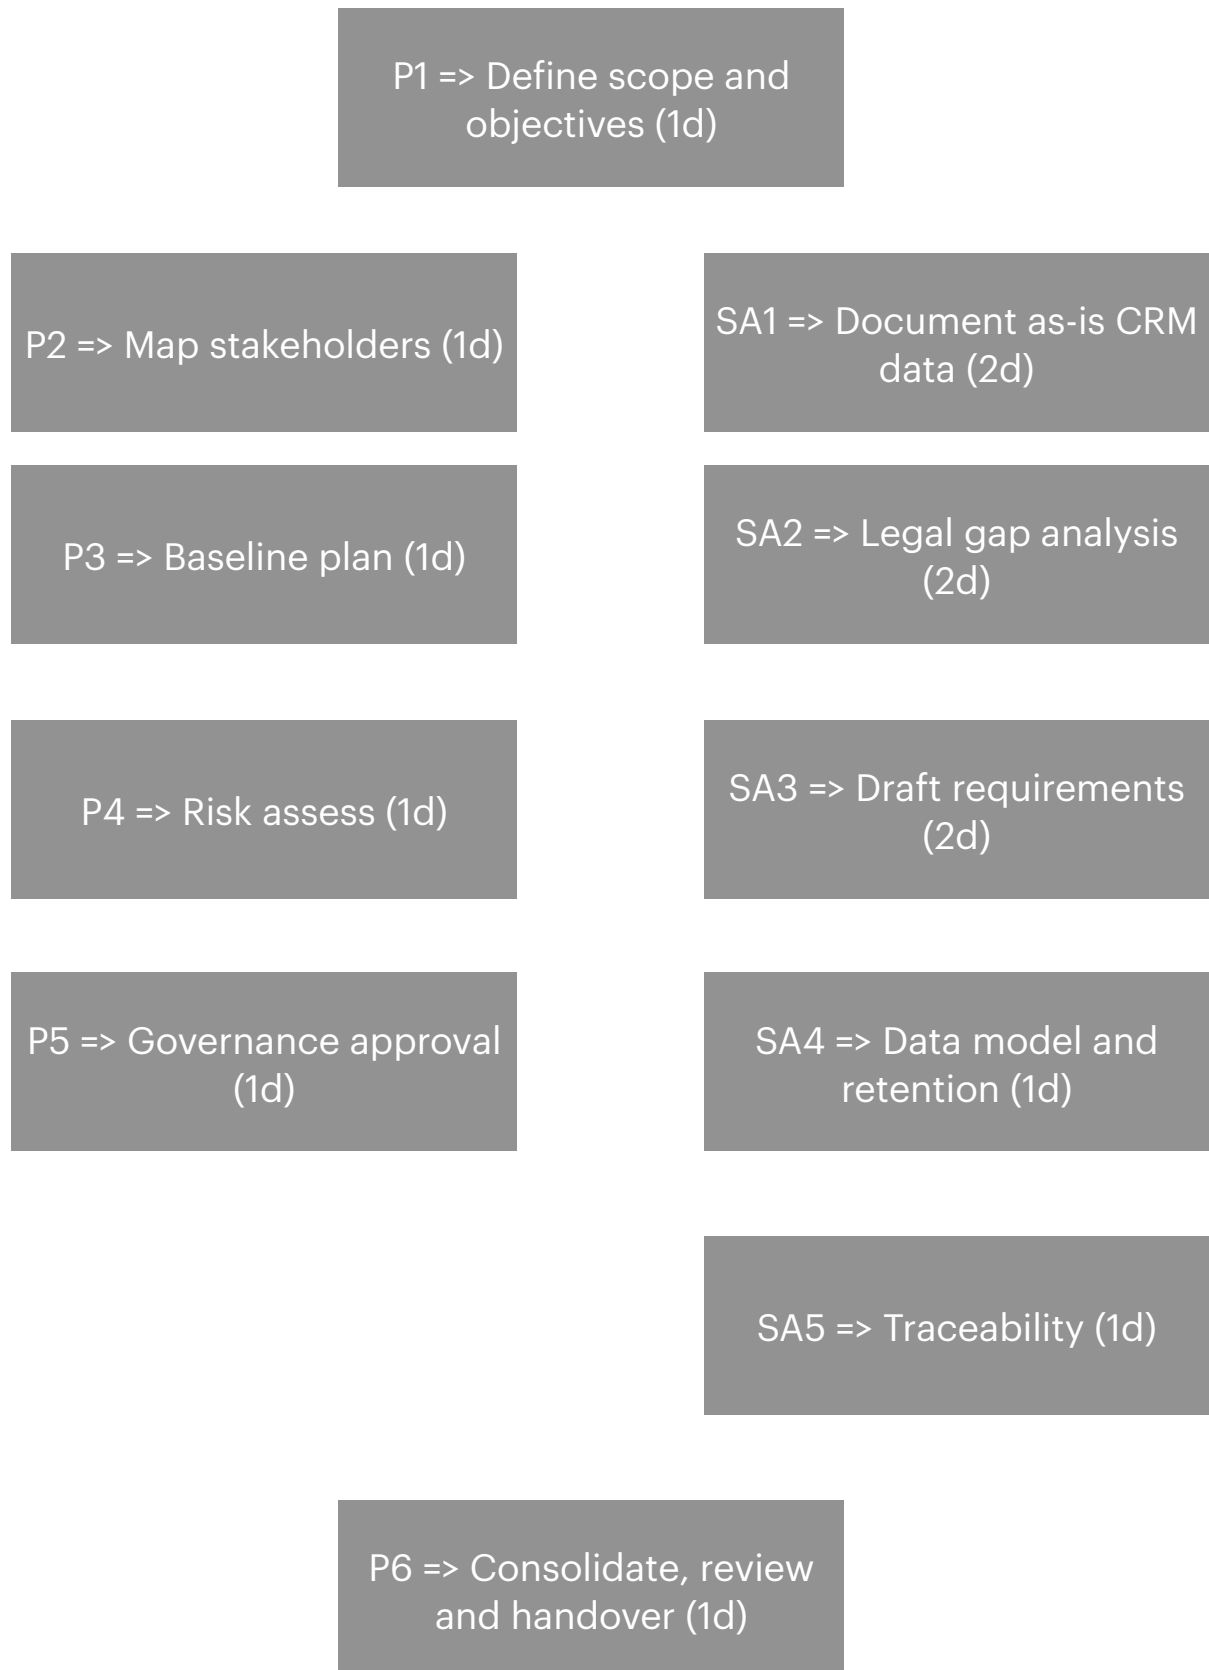

Critical Path Analysis

ID	Team	Duration	ES	EF	LS	LF	Slack	Critical
P1	Project	1	0	1	0	1	0	Yes
P2	Project	1	1	2	5	6	4	No
P3	Project	1	2	3	6	7	4	No
P4	Project	1	2	3	6	7	4	No
P5	Project	1	3	4	7	8	4	No
SA1	Product	2	1	3	1	3	0	Yes
SA2	Product	2	3	5	3	5	0	Yes
SA3	Product	2	5	7	5	7	0	Yes
SA4	Product	1	7	8	7	8	0	Yes
SA5	Product	1	7	8	7	8	0	Yes
P6	Project	1	8	9	8	9	0	Yes

Kanban “Screenshot”

To Do	In Progress	Done
SA4		P1
SA5		P2
P6		P3
		P4
		P5
		SA1
		SA2
		SA3
