

Sprint 2 Burndown Chart

Software Engineering - SVNC.00.308

Project: StayEase Hotel Reservation System

Team: Cat Bacillus (Kyrylo Pryiomyshev, Danylo Chernov, Daniil Ustuhov)

Date: March 9, 2026

Version: 1.0

Project Name: StayEase Hotel Reservation System
Team: Cat Bacillus (Kyrylo Pryiomyshhev, Danylo Chernov, Daniil Ustihov)
Sprint Number: 2
Sprint Duration: 90 minutes (Lecture 7 + Lecture 8)
Date: March 9, 2026

Sprint 2 Overview

Stories Committed: US-05, US-06, US-07, US-09 (16 story points)
Stories Completed: US-05, US-06, US-07, US-09 (16 story points)
Sprint Goal: Complete double-booking prevention, enable cancellation and history, deliver staff dashboard
Adjusted Velocity: Based on Sprint 1 actual completion of 18 points; committed to 16 for safety margin


Retrospective Improvements Applied

- Reduced commitment from 21 to 16 points (velocity-based planning)
- Testing distributed across all team members (each developer tests own feature)
- US-05 re-estimated from S(3) to M(5) after identifying concurrency complexity

Progress Data

Time	Completed Work	Remaining Points	Notes
Start (0 min)	Nothing yet	16 points	Sprint begins with adjusted capacity
30 min	US-05 (Double Booking Prevention) completed	11 points	Carried story resolved first
60 min	US-06 (Cancel Reservation) completed	6 points	On track, zero bugs found
90 min (End)	US-07 (History) and US-09 (Dashboard) completed	0 points	All stories done, 10 min to spare

Burndown Chart

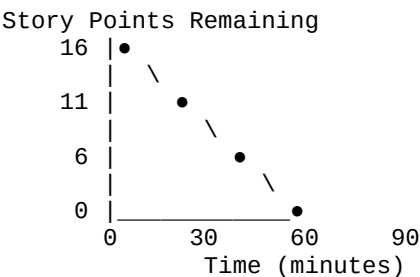

Legend: ● = Actual \ = Ideal burndown

Interpretation

The actual burndown closely followed the ideal line throughout Sprint 2, demonstrating significantly improved estimation accuracy compared to Sprint 1. All four committed stories were completed within the 90-minute timebox with approximately 10 minutes remaining. This improvement is directly attributable to the Sprint 1 retrospective action items: velocity-based planning removed overcommitment pressure, distributed testing eliminated bottlenecks, and re-estimating US-05 prevented a repeat of the underestimation problem. Sprint 2 velocity of 16 points matched the commitment exactly.

Daily Standup Notes

Standup 2 (Lecture 7, Start of Sprint 2)

Member	Completed (Sprint 1)	Working On Today	Blockers
Kyrylo	US-01 API, US-03 API, US-04 API, US-05 partial	Transaction locking (US-05), Cancel API (US-06)	None
Danylo	US-01 UI, US-02, US-03 UI, US-04 UI	Alt room suggestions (US-05), Cancel button (US-06)	None
Daniil	Tested US-01 to US-04	Concurrent booking tests (US-05), Cancel edge cases (US-06)	None

Standup 3 (Lecture 8, Start of Day 2)

Member	Completed Yesterday	Working On Today	Blockers
Kyrylo	US-05 locking, US-06 Cancel API	History API (US-07), Dashboard API (US-09)	None
Danylo	US-05 alt suggestions UI, US-06 Cancel button	My Reservations (US-07), Dashboard UI (US-09)	None
Daniil	Tested US-05 and US-06	Integration tests for US-07 and US-09	None

Task Board (End of Sprint 2)

To Do	In Progress	Done
(empty)	(empty)	US-05: Transaction locking + Alt suggestions + Tests
		US-06: Cancel API + Cancel button + Edge case tests
		US-07: History API + My Reservations page + Tests

		US-09: Dashboard API + Dashboard UI + Tests
--	--	--

Sprint 2 Result: 4 of 4 stories completed (16/16 points). Sprint commitment fully met.
